Risks list

https://fujitsu.tpondemand.com/RestUI/Board.aspx#page=board/539838112130355953 1&appConfig=eyJhY2lkIjoiODkyMzM4ODAzQ0E0MTE2NzM3NkZGQjEzRkJBOUZFNk...

Fujitsu | Welcome to Fujitsu... | Apps Dev Team... | Services Hub | https://fujitsueur-... | Opportunity Mark... | Microsoft Certified:... | Microsoft Certified:... | Study guide for Ex... | Console Home | C...

Find entities by text or id

Solutions

Risks list

Filter cards off | Global Delivery Portfolio | GDU Apps Dev ART | Any Planning Interval | Any Tag | Apps SAP Integration Standardization... | Actions

TEAMS | ID | Icon | People | Portfolios

Apps SAP Integration Standardization | 376196 | +17 | Off

RISKS	Issue	State	Level	ROAM	Responsible	Risk Actions	Created	Accountable Team	Creator Name	Teams	Last Commented	All relations	Description
Lack of Product Owner for SAP Team		DONE	Team	Accepted	Tarun Tyagi		5 Dec 2025	Apps SAP Inte...	Aleksandra Wojewoda		22 Jan 2026		There is a risk that the SAP Teams progress and PI Planning/Execution will be hindered which is caused by not
Low regional adoption		OPEN	Team	Accepted	Pramod Tyagi		11 Dec 2025	Apps SAP Inte...	Aleksandra Wojewoda		10 Mar 2026		There is a significant risk that any newly created standardized assets will not be adopted by the regions, similar
Approval Delay Impacts on GDU's Scope		IN PROGRESS	Team	Accepted	Pramod Tyagi		12 Jan 2026	Apps SAP Inte...	Aleksandra Wojewoda		19 Mar 2026	4	During PI Planning, the team identified a risk related to the current approval process for documentation and ac
Translator required		IN PROGRESS	Team	Owned	Pramod Tyagi		30 Mar 2026	Apps SAP Inte...	Aleksandra Wojewoda		19 Mar 2026	1	
Inadequate Resourcing for Activity Complet...		IN PROGRESS	ART PI	Accepted	Pramod Tyagi		19 Mar 2026	Apps SAP Inte...	Aleksandra Wojewoda		19 Mar 2026	1	There is a risk that planned deliverables will be delayed or incomplete which is caused by lack of dedicated bu

1 - 1 of 1

Entities per page: 20 50 200 500

Risks list

https://fujitsu.tpondemand.com/RestUI/Board.aspx#page=board/539838112130355953 1&appConfig=eyJhY2lkIjoiODkyMzM4ODAzQ0E0MTE2NzM3NkZGQjEzRlJBOUZFNk...

Fujitsu | Welcome to Fujitsu... | Apps Dev Team... | Services Hub | https://fujitsuear-... | Opportunity Mark... | Microsoft Certified:... | Microsoft Certified:... | Study guide for Ex... | Console Home | C...

Find entities by text or id | Solutions

Risks list | Filter cards | Global Delivery Portfolio | GDU Apps Dev ART | Any Planning Interval | Any Tag | Apps SAP Integration Standardization... | Actions

Attributes	Description	There is a risk that	Which is caused by	Resulting in
	There is a risk that the SAP Team's progress and PI Planning Execution will be hindered which is caused by not h...	the SAP Team's progress and PI Planning Execution will be hindered	not having a Product Owner assigned to the team	backlog managemen
	There is a significant risk that any newly created standardized assets will not be adopted by the regions, similar t...	any newly created standardized assets will not be adopted by the regions, similar to the existing Bluefield conte...	not enough promotion and visibility among regions	not consistency in de
4	During PI Planning, the team identified a risk related to the current approval process for documentation and acc...	we will not deliver our (GDUs) scope	time consuming approval process	delays in delay with P
1		Team will not be able to provide English version of SAP IMS Private Cloud templates on time	lack of bilingual (Japanese-English) person to run the quality check after machine translation	blocking the SMEs a
1	There is a risk that planned deliverables will be delayed or incomplete which is caused by lack of dedicated budg...	planned deliverables will be delayed or incomplete	(1) lack of dedicated budget/ Project Code from SLM for this activity and (2) insufficient available team time to...	a failure to meet proj

1 - 1 of 1 | Entities per page 20 50 100 500

Risks list

https://fujitsu.tpondemand.com/RestUI/Board.aspx#page=board/539838112130355953 1&appConfig=eyJhY2lkIjoiODkyMzM4ODAzQ0E0MTE2NzM3NkZGQjEzRlJBOUZFNk...

Fujitsu | Welcome to Fujitsu... | Apps Dev Team... | Services Hub | https://fujitsuear-... | Opportunity Mark... | Microsoft Certified:... | Microsoft Certified:... | Study guide for Ex... | Console Home | C...

Find entities by text or id | Solutions

Risks list | Filter cards | Global Delivery Portfolio | GDU Apps Dev ART | Any Planning Interval | Any Tag | Apps SAP Integration Standardization... | Actions

There is a risk that	Which is caused by	Resulting in	Likelihood	Likelihood value	Impact	Impact value	Likelihood x
the SAP Team's progress and PI Planning Execution will be hindered	not having a Product Owner assigned to the team	backlog management being handled by others and slowing over all progress	3-Medium	3	5-High	5	15
any newly created standardized assets will not be adopted by the regions, similar to the existing Bluefield conte...	not enough promotion and visibility among regions	not consistency in delivery standards	1-Low	1	1-Low	1	1
we will not deliver our (GDUs) scope	time consuming approval process	delays in delay with PI IS objective delivery	3-Medium	3	3-Medium	3	9
Team will not be able to provide English version of SAP IMS Private Cloud templates on time	lack of bilingual (Japanese-English) person to run the quality check after machine translation	blocking the SMEs activities and creating delays in expected project timeline.	3-Medium	3	3-Medium	3	9
planned deliverables will be delayed or incomplete	(1) lack of dedicated budget/ Project Code from SLM for this activity and (2) insufficient available team time to...	a failure to meet project timelines and objectives	3-Medium	3	3-Medium	3	9

1 - 1 of 1 | Entities per page 20 50 100 500

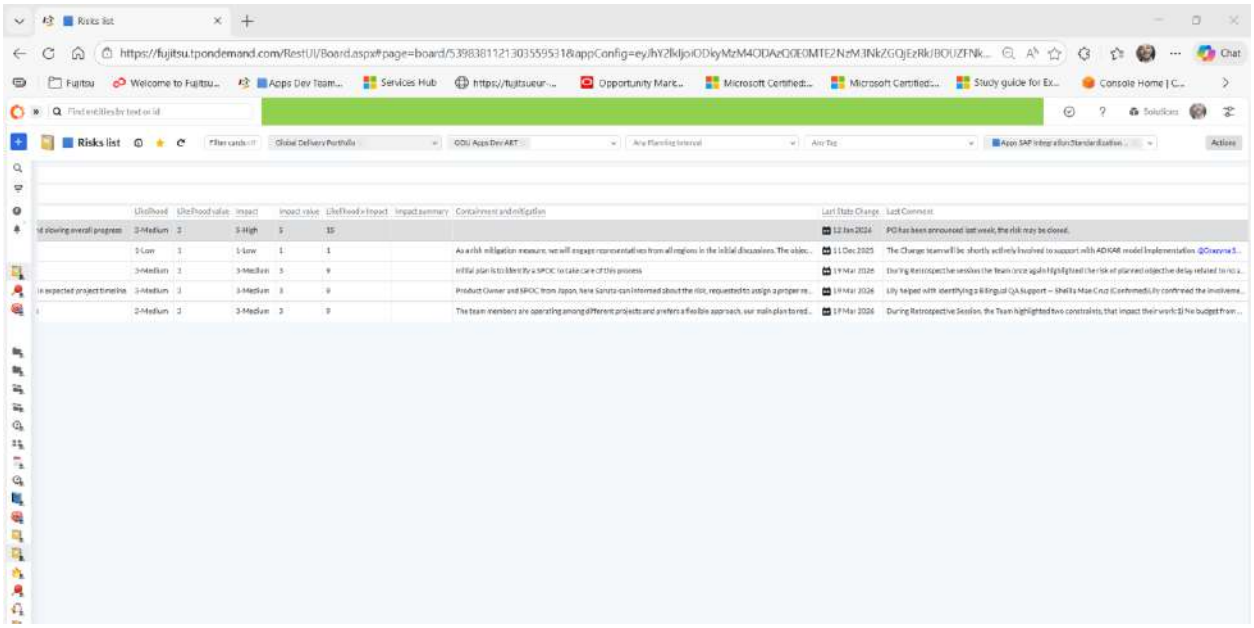
Risks list
Risks list
Likelihood
Likelihood value
Impact
Impact value
Likelihood x Impact
Impact summary
Containment and mitigation
Last State Change
Last Comment

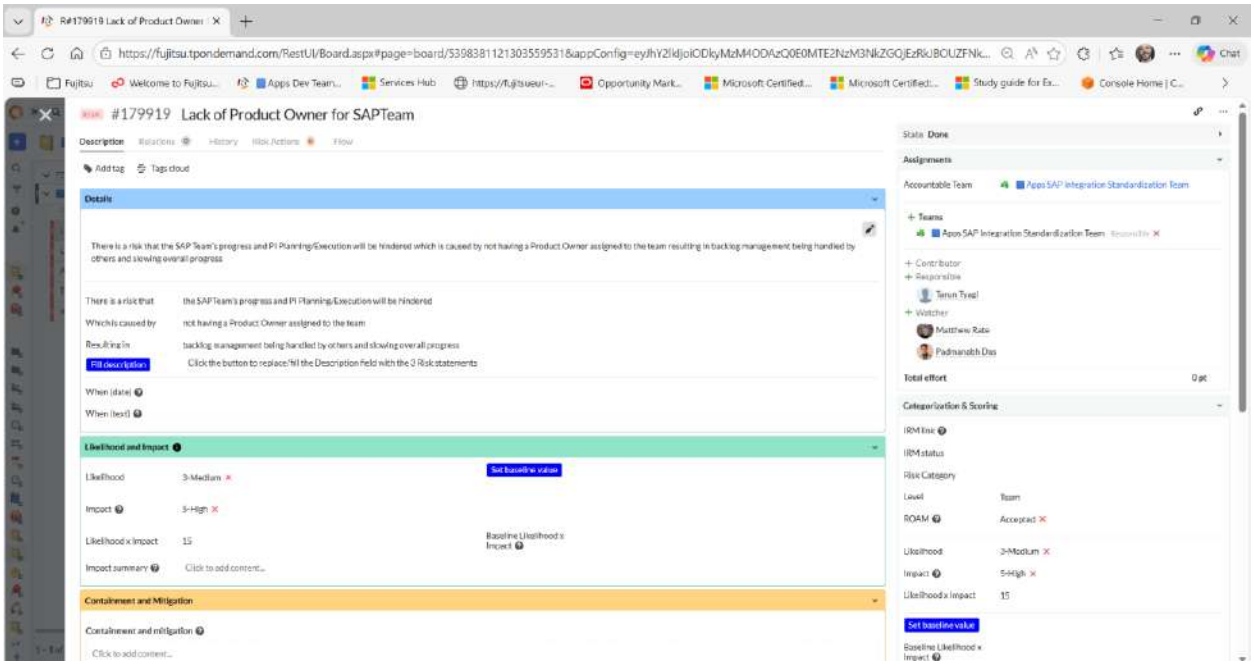
#179919 Lack of Product Owner for SAPTeam
Description
Add tag
Tags cloud
Details
There is a risk that the SAP Team's progress and PI Planning/Execution will be hindered which is caused by not having a Product Owner assigned to the team resulting in backlog management being handled by others and slowing overall progress
There is a risk that
the SAPTeam's progress and PI Planning/Execution will be hindered
Which is caused by
not having a Product Owner assigned to the team
Resulting in
backlog management being handled by others and slowing overall progress
Fill description
Click the button to replace/fill the Description field with the 3 Risk statements
When (date)
When (text)
Likelihood and Impact
Likelihood
3-Medium
Impact
5-High
Likelihood x Impact
15
Impact summary
Click to add content...
Set baseline value
Baseline Likelihood x Impact
Containment and Mitigation
Containment and mitigation
Click to add content...
State Done
Assignments
Accountable Team
Apps SAP Integration Standardization Team
Teams
Contributor
Responsible
Tenin Tyrel
Watcher
Matthew Rabe
Padmanabh Das
Total effort
0 pt
Categorization & Scoring
IRM Esc
IRM status
Risk Category
Level
Team
ROAM
Accepted
Likelihood
3-Medium
Impact
5-High
Likelihood x Impact
15
Set baseline value
Baseline Likelihood x Impact

RA179919 Lack of Product Owner

https://fujitsu.tpondemand.com/RestUI/Board.aspx#page=board/539838112130355953 1&appConfig=eyJhY2lkIjoiODkyMzM4ODAzQ0E0MTE2NzM3NkZGQjEzRkJBOUZFNk...

Fujitsu | Welcome to Fujitsu... | Apps Dev Team... | Services Hub | https://fujitsueur-... | Opportunity Mark... | Microsoft Certified:... | Microsoft Certified:... | Study guide for Ex... | Console Home | C...

Impact summary — Click to add content...

Containment and Mitigation

Containment and mitigation

Click to add content...

Containment or mitigation failure actions

Click to add content...

Data quality management

Criteria Check Results HTML

- Incomplete risks
  - ContainmentAndMitigationFieldsFilled check
- Old risks
  - PlanningIntervalFieldsLinkedToCurrentOrFuturePI check

Drag and drop files here or click to select files

Comments

Aleksandra Wojewoda
PO has been announced last week, the risk may be closed.

+ Add comment

Impact: 5 High

Likelihood x Impact: 15

Set baseline value

Baseline Likelihood x Impact

Issue

Info

Portfolio: Global Delivery Portfolio

Creator: Aleksandra Wojewoda

Creation date: 5 Dec 2025

Entity selection:

Select the entity this risk is for using one of the options below. Use Other only if the other entity types are not appropriate

Portfolio Epic

Epic

Story

Planning Interval: 164406 Apps PI5

Team Iteration

Other

ROAM: Accepted

Level: Team

Issue

Data quality management details

RK180546 Low regional adoption

https://fujitsu.tpondemand.com/RestUI/Board.aspx#page=board/539838112130355953 1&appConfig=eyJhY2lkIjoiODkyMzM4ODAzQ0E0MTE2NzM3NkZGQjEzRkJBOUZFNk...

Fujitsu | Welcome to Fujitsu... | Apps Dev Team... | Services Hub | https://fujitsueur-... | Opportunity Mark... | Microsoft Certified:... | Microsoft Certified:... | Study guide for Ex... | Console Home | C...

RISK #180546 Low regional adoption

Description | Relations | History | Risk Actions | Flow

Add tag | Tags cloud

Details

- There is a significant risk that any newly created standardized assets will not be adopted by the regions, similar to the existing Bluefield content. A clear promotion and communication plan is needed.

There is a risk that	any newly created standardized assets will not be adopted by the regions, similar to the existing Bluefield content. A clear promotion and communication plan is needed.
Which is caused by	not enough promotion and visibility among regions
Resulting in	not consistency in delivery standards
Fill description	Click the button to replace/fill the Description field with the 3 Risk statements
When (date)	
When (text)	

Likelihood and Impact

Set baseline value

Likelihood	1-Low	
Impact	1-Low	
Likelihood x Impact	1	Baseline Likelihood x Impact
Impact summary	Click to add content...	

Containment and Mitigation

Containment and mitigation

State: Open

Assignments

Accountable Team: Apps SAP Integration Standardization Team

+ Teams: Apps SAP Integration Standardization Team

+ Contributor: Grazyna Swidorsk, Weronika Nicinska

+ Responsible: Pramod Tyagi

+ Watcher: Aleksandra Wojewoda

Total effort: 0 pt

Categorization & Scoring

IRM link	
IRM status	
Risk Category	
Level	Team
ROAM	Accepted
Likelihood	1-Low
Impact	1-Low
Likelihood x Impact	1

Set baseline value

RK180546 Low regional adoption

https://fujitsu.tpondemand.com/RestUI/Board.aspx#page=board/539838112130355953 1&appConfig=eyJhY2lkIjoiODkyMzM4ODAzQ0E0MTE2NzM3NkZGQjEzRkJBOUZFNk...

Fujitsu | Welcome to Fujitsu... | Apps Dev Team... | Services Hub | https://fujitsueur-... | Opportunity Mark... | Microsoft Certified:... | Microsoft Certified:... | Study guide for Ex... | Console Home | C...

Impact summary | Click to add content...

Containment and Mitigation

Containment and mitigation

As a risk mitigation measure, we will engage representatives from all regions in the initial discussions. The objective is to secure their consensus and formal acknowledgment of the defined set of minimum standards.

Containment or mitigation failure actions

If an agreement cannot be reached, the matter will be escalated to senior leadership for clear direction.

Data quality management

All quality criteria are OK.

Drag and drop files here or click to select files

Comments — Oldest first | Newest first

Aleksandra Wojewoda Dec 11, 2025 at 01:28 PM 3 months ago (edited)
the potential risk has been raised during SAP Japan SLM Integration Standardization - Sync Working Group weekly meeting by Nuno, who had previous experience in the subject

Aleksandra Wojewoda Jul 22, 2026 at 07:23 AM 2 months ago
As the Product Owner has only been announced last week, this risk was just taken into PO's attention.

Aleksandra Wojewoda Feb 22, 2026 at 06:33 AM last month
No promotion is needed until the final product is ready.

Aleksandra Wojewoda Mar 12, 2026 at 09:28 AM 6 days ago
The Change team will be shortly actively involved to support with ADKAR model implementation
@ Grazyna Swidorsk and @ Weronika Nicinska FYI for the moment.

+ Add comment

Impact: 1-Low

Likelihood x Impact: 1

Set baseline value

Baseline Likelihood x Impact

Issue

Info

Portfolio	Global Delivery Portfolio
Creator	Aleksandra Wojewoda
Creation date	11-Dec-2025

Entity selection:

Select the entity this risk is for using one of the options below. Use Other only if the other entity types are not appropriate

Portfolio Epic	
Epic	
Story	
Planning Interval	184406 Apps PI5
Team Iteration	
Other	
ROAM	Accepted
Level	Team
Issue	

Data quality management details

R#182698 Approval Delay Impacts

https://fujitsu.tpondemand.com/RestUI/Board.aspx#page=board/539838112130355953 1&appConfig=eyJhY2lkIjoiODkyMzM4ODAzQ0E0MTE2NzM3NkZGQjEzRkJBOUZFNk...

Fujitsu | Welcome to Fujitsu... | Apps Dev Team... | Services Hub | https://fujitsueur-... | Opportunity Mark... | Microsoft Certified:... | Microsoft Certified:... | Study guide for Ex... | Console Home | C...

#182698 Approval Delay Impacts on GDUs Scope

Description | Relations | History | Risk Actions | Files

Add tag | Tags cloud

Details

During PI Planning, the team identified a risk related to the current approval process for documentation and access of existing materials on JGG side.
Specifically for agreeing upon a minimum set of document templates and access to critical JGG documents was highlighted as time-consuming.

There is a risk that	we will not deliver our (GDUs) scope
Which is caused by	time-consuming approval process
Resulting in	delays in delay with PI5 objective delivery

Fill description — Click the button to replace/fill the Description field with the 3 Risk statements

When (date)

When (text)

Likelihood and Impact

Set baseline value

Likelihood	3-Medium		
Impact	3-Medium		
Likelihood x Impact	9	Baseline Likelihood x Impact	3

Impact summary — Click to add content...

Containment and Mitigation

Containment and mitigation

State: In Progress

Assignments

Accountable Team: Apps SAP Integration Standardization Team

Teams: Apps SAP Integration Standardization Team

Contributor: Saruta Kanji

Responsible: Pramod Tyagi

Watcher

Total effort: 0 pt

Categorization & Scoring

IRM link	
IRM status	
Risk Category	
Level	Team
ROAM	Accepted
Likelihood	3-Medium
Impact	3-Medium
Likelihood x Impact	9

Set baseline value

Baseline Likelihood x Impact: 3

R#182698 Approval Delay Impacts

https://fujitsu.tpondemand.com/RestUI/Board.aspx#page=board/539838112130355953 1&appConfig=eyJhY2lkIjoiODkyMzM4ODAzQ0E0MTE2NzM3NkZGQjEzRkJBOUZFNk...

Fujitsu | Welcome to Fujitsu... | Apps Dev Team... | Services Hub | https://fujitsueur-... | Opportunity Mark... | Microsoft Certified:... | Microsoft Certified:... | Study guide for Ex... | Console Home | C...

Likelihood x Impact: 9 — Baseline Likelihood x Impact: 3

Impact summary — Click to add content...

Containment and Mitigation

Containment and mitigation

Initial plan is to identify a SPOC to take care of this process

Containment or mitigation failure actions

Click to add content...

Data quality management

All quality criteria are OK.

Drag and drop files here or click to select files

Comments — Oldest first | Newest first

Aleksandra Wojewoda
As advised by Lily the case should be discussed with vamadu.vyasi@fujitsu.com and/or gacujin@fujitsu.com by Pramod Tyagi

Aleksandra Wojewoda
It has been again re-emphasized that there is a risk of potential project delays due to longer approval timelines aligned with local practices, as well as the current availability of Japan-specific SAP Activate methodology templates.

Yuliya Stanevich
The export control is completed. Confirmed on 26/02/2026

Aleksandra Wojewoda
During Retrospective session the Team once again highlighted the risk of planned objective delay related to no agreement on minimum list of templates from Japan.

+ Add comment

Impact	3-Medium
Likelihood x Impact	9

Set baseline value

Baseline Likelihood x Impact: 3

Issue

Info

Portfolio	Global Delivery Portfolio
Creator	Aleksandra Wojewoda
Creation date	12-Jan-2026

Entity selection:

Select the entity this risk is for using one of the options below. Use Other only if the other entity types are not appropriate

Portfolio Epic	
Epic	
Story	
Planning Interval	164495 Apps PI5
Team Iteration	1021647 Apps PI5 Iteration 3
Other	
ROAM	Accepted
Level	Team
Issue	

Data quality management details

RK188899 Translator required

https://fujitsu.tpondemand.com/RestUI/Board.aspx#page=board/539838112130355953 1&appConfig=eyJhY2lkIjoiODkyMzM4ODAzQ0E0MTE2NzM3NkZGQjEzRlkJBOUZFNk...

Fujitsu | Welcome to Fujitsu... | Apps Dev Team... | Services Hub | https://fujitsueur-... | Opportunity Mark... | Microsoft Certified:... | Microsoft Certified:... | Study guide for Ex... | Console Home | C...

RISK #188899 Translator required

Description | Relations | History | Risk Actions | Flow

Add tag | Tags cloud

Details

Click to add description...

There is a risk that: Team will not be able to provide English version of SAP IMS Private Cloud templates on time

Which is caused by: lack of bilingual (Japanese-English) person to run the quality check after machine-translation

Resulting in: blocking the SMEs activities and creating delays in expected project timeline.

Fill description: Click the button to replace/fill the Description field with the 3 Risk statements

When (date)

When (text)

Likelihood and Impact

Likelihood: 3-Medium | Set baseline value

Impact: 3-Medium

Likelihood x Impact: 9 | Baseline Likelihood x Impact

Impact summary: Click to add content...

Containment and Mitigation

Containment and mitigation

Product Owner and SPOC from Japan, here Saruta-san informed about the risk, requested to assign a proper resource to support with translation.

State: In Progress

Assignments

Accountable Team: Apps SAP Integration Standardization Team

Teams: Apps SAP Integration Standardization Team

Contributor

Responsible: Pramod Tyagi

Watcher

Total effort: 0 pt

Categorization & Scoring

IRM link

IRM status

Risk Category

Level: Team

ROAM: Owned

Likelihood: 3-Medium

Impact: 3-Medium

Likelihood x Impact: 9

Set baseline value

Baseline Likelihood x Impact

Issue

RK188899 Translator required

https://fujitsu.tpondemand.com/RestUI/Board.aspx#page=board/539838112130355953 1&appConfig=eyJhY2lkIjoiODkyMzM4ODAzQ0E0MTE2NzM3NkZGQjEzRlkJBOUZFNk...

Likelihood x Impact: 9

Impact summary: Click to add content...

Containment and Mitigation

Containment and mitigation

Product Owner and SPOC from Japan, here Saruta-san informed about the risk, requested to assign a proper resource to support with translation.

Containment or mitigation failure actions

Click to add content...

Data quality management

Criteria Check Results HTML

- Old risks
  - PlanninInterval FieldsFilled check
  - PlanninInterval FieldsLinkedToCurrentOrFuturePI check

Drag and drop files here or click to select files

Comments | Oldest first | Newest first

Aleksandra Wojewoda Mar 11, 2026 at 10:45 AM (1 day ago)

Pramod requested via e-mail to collaborate with Nilesh Dodo and Seino-san to secure the necessary resource for translation

Aleksandra Wojewoda Mar 19, 2026 at 07:27 AM (1 hour ago)

Lily helped with identifying a Bilingual QA Support – Sheila Mae Cruz (Confirmed) Lily confirmed the involvement of Sheila Mae Cruz (s.cruz@fujitsu.com), who has direct experience with the Zimrai tool and is a bilingual Japanese/English speaker at N1 level.

Add comment

Impact: 3-Medium

Likelihood x Impact: 9

Set baseline value

Baseline Likelihood x Impact

Issue

Info

Portfolio: Global Delivery Portfolio

Creator: Aleksandra Wojewoda

Creation date: 10-Mar-2026

Entity selection:

Select the entity this risk is for using one of the options below. Use Other only if the other entity types are not appropriate.

Portfolio Epic

Epic

Story

Planning Interval

Team Iteration

Other

ROAM: Owned

Level: Team

Issue

Data quality management details

R#189658 Inadequate Resourcing

https://fujitsu.tpondemand.com/RestUI/Board.aspx#page=board/539838112130355953 1&appConfig=eyJhY2lkIjoiODkyMzM4ODAzQ0E0MTE2NzM3NkZGQjEzRkJBOUZFNk...

Fujitsu | Welcome to Fujitsu... | Apps Dev Team... | Services Hub | https://fujitsueur-... | Opportunity Mark... | Microsoft Certified:... | Microsoft Certified:... | Study guide for Ex... | Console Home | C...

RISK #189658 Inadequate Resourcing for Activity Completion

Description | Relations | History | Risk Actions | Flow

Add tag | Tags cloud

Details

There is a risk that planned deliverables will be delayed or incomplete which is caused by lack of dedicated budget/ Project Code from SLM for this activity causing insufficient available team time to work on the deliverables resulting in a failure to meet project timelines and objectives

There is a risk that: planned deliverables will be delayed or incomplete

Which is caused by: (1) lack of dedicated budget/ Project Code from SLM for this activity and (2) Insufficient available team time to work on the deliverables

Resulting in: a failure to meet project timelines and objectives

Fill description — Click the button to replace/fill the Description field with the 3 Risk statements

When (date)

When (text)

Likelihood and Impact

Set baseline value

Likelihood: 3-Medium

Impact: 3-Medium

Likelihood x Impact: 9

Baseline Likelihood x Impact

Impact summary: Click to add content...

Containment and Mitigation

Containment and mitigation

State: In Progress

Assignments

Accountable Team: Apps SAP Integration Standardization Team

Teams: Apps SAP Integration Standardization Team

Contributor

Responsible: Pramod Tyagi

Watcher: Matthew Rate, Padmanabh Das

Total effort: 0pt

Categorization & Scoring

IRM Risk

IRM status

Risk Category

Level: ART PI

ROAM: Accepted

Likelihood: 3-Medium

Impact: 3-Medium

Likelihood x Impact: 9

Set baseline value

Baseline Likelihood x Impact

R#189658 Inadequate Resourcing

https://fujitsu.tpondemand.com/RestUI/Board.aspx#page=board/539838112130355953 1&appConfig=eyJhY2lkIjoiODkyMzM4ODAzQ0E0MTE2NzM3NkZGQjEzRkJBOUZFNk...

Fujitsu | Welcome to Fujitsu... | Apps Dev Team... | Services Hub | https://fujitsueur-... | Opportunity Mark... | Microsoft Certified:... | Microsoft Certified:... | Study guide for Ex... | Console Home | C...

Impact summary: Click to add content...

Containment and Mitigation

Containment and mitigation

The team members are operating among different projects and prefers a flexible approach, our main plan to reduce this risk is to align and prioritize our work with their other duties.
This helps the team stay self organized and ensures important tasks are handled, all without forcing a full Scrum process.

Containment or mitigation failure actions

Click to add content...

Data quality management

Criteria Check Results HTML

- Old risks
  - PlanningIntervalFieldIsFilled check
  - PlanningIntervalFieldsLinkedToCurrentOrFuturePI check

Drag and drop files here or click to select files

Comments

Aleksandra Wojowoda

During Retrospective Session, the Team highlighted two constraints, that impact their work:
1) **No budget from SLM for this activity:** This directly impacts the ability to procure resources (human or other) for the activity.
2) **Lack of available time to work on the deliverables:** This is due to existing commitments vs. objectives timelines

Add comment

Impact: 3-Medium

Likelihood x Impact: 9

Set baseline value

Baseline Likelihood x Impact

Issue

Info

Portfolio: Global Delivery Portfolio

Creator: Aleksandra Wojewoda

Creation date: 19-Mar-2026

Entity selection:

Select the entity this risk is for using one of the options below. Use Other only if the other entity types are not appropriate

Portfolio Epic

Epic

Story

Planning Interval

Team Iteration

Other

ROAM: Accepted

Level: ART PI

Issue

Data quality management details
